

REPORT

Phase 7 - Woodsmith Mine Noise and Vibration Management Plan

Woodsmith Mine Phase 7 - NVMP

Client: Sirius Minerals plc

Reference: 40-RHD-WS-70-EN-PL-0030_Rev1

Revision: 01/Final

Date: 28 August 2018

HASKONINGDHV UK LTD.

Marlborough House
Marlborough Crescent
Newcastle upon Tyne
NE1 4EE
Industry & Buildings
VAT registration number: 792428892

Document title: Phase 7 - Woodsmith Mine Noise and Vibration Management Plan

Document short title: PHASE 7 WOODSMITH MINE NOISE AND VIBRATION MANAGEMENT PLAN

Reference: 40-RHD-WS-70-EN-PL-0030_Rev1

Revision: 01/Final

Date: 28 August 2018

Project name: Sirius North Yorkshire Polyhalite Project

Project number: PB1110

Author(s): Stephen Wigham

Drafted by: Stephen Wigham

Checked by: Dean Curtis

Date / initials: 28 August 2018 / DC

Approved by: Matthew Hunt

Date / initials: 28 August 2018 / MH

Classification

Project related



Disclaimer

No part of these specifications/printed matter may be reproduced and/or published by print, photocopy, microfilm or by any other means, without the prior written permission of HaskoningDHV UK Ltd.; nor may they be used, without such permission, for any purposes other than that for which they were produced. HaskoningDHV UK Ltd. accepts no responsibility or liability for these specifications/printed matter to any party other than the persons by whom it was commissioned and as concluded under that Appointment. The integrated QHSE management system of HaskoningDHV UK Ltd. has been certified in accordance with ISO 9001:2015, ISO 14001:2015 and OHSAS 18001:2007.

Table of Contents

1	INTRODUCTION	1
1.1	Purpose of this Report	1
2	GUIDANCE	3
2.1	Legislation and British Standards	3
2.2	Construction Limits	3
2.3	Construction Method	3
3	PREDICTED CONSTRUCTION NOISE AND VIBRATION LEVELS	4
3.1	Baseline Receptor Locations	4
3.2	Predicted Noise Levels	4
3.3	Vibration	4
4	NOISE MONITORING PROGRAMME	5
4.1	Noise Monitoring	5
5	MITIGATION AND PROCEDURES	5
5.1	Purpose of the Section	5
5.2	Best Practice Measures	5
5.3	Specific Mitigation	6
5.4	Communications	6

Table of Tables

Table 1-1:	Condition NYMNPA 18 Noise and Vibration Management Plan	1
------------	---	---

Appendices

Appendix A	Acoustic Terminology
Appendix B	Figures
Appendix C	Predicted Construction Noise Levels



Document Sign-Off

This document forms the Noise and Vibration Management Plan (NVMP) to address construction works associated with the Phase 7 Works at Woodsmith Mine. The NVMP was produced to address the requirements of Planning Condition NYMNPA-18.

The Contractor(s) commit(s) to comply with all noise and vibration management approaches and procedures detailed herein.

.....
(Contractor)

.....
(Date)

The remainder of this document contains technical information to support the NVMP and address the requirements of the Planning Condition. The document may be revised and updated as the project progresses.

1 INTRODUCTION

1.1 Purpose of this Report

- 1.1.1 In 2014 a planning application (reference NYM/2014/0676/MEIA) was submitted to North York Moors National Park Authority (NYMNPA) for permission to develop a polyhalite mine and underground Mineral Transport System (MTS). Planning permission was subsequently granted in 2015 subject to conditions, as varied in February 2018 by NYM/2017/0505/MEIA.
- 1.1.2 This document has been prepared on behalf of Sirius Minerals plc (Sirius Minerals) and details the requirements with respect to noise and vibration management for the Phase 7 Works (see Paragraph 1.1.4 below) at Woodsmith Mine. This document is required to partially satisfy the requirements of Condition 18 of the NYMNPA planning permission. It has been prepared in accordance with current good practice. This planning condition states that:

Table 1-1: Condition NYMNPA 18 Noise and Vibration Management Plan

NYMNPA 18	Compliance with Condition NYMNPA-18
Prior to the commencement of the development at Dove's Nest Farm or Lady Cross Plantation, a Noise and Vibration Management Plan (NVMP) for the control, mitigation and monitoring of noise and vibration for both construction and operational phases at the two sites shall be submitted to and approved in writing by the MPA in consultation with the SBC EHO. The scheme shall set out the following:	This document addresses Phase 7 Works at Woodsmith Mine. Works at Lady Cross Plantation are deferred and are therefore not addressed in this Plan.
Noise-sensitive receptors for which predictions shall be made and at which the noise and vibration limits shall apply and which shall include recreational receptors.	Section 3.1
Predicted noise levels at the noise-sensitive receptors from noise and vibration generated at the DNF and LCP sites for the key construction phases during the forthcoming year including any periods in which the higher daytime limit of 70 dB L_{Aeq} shall apply (permitted 56 days for temporary works to create noise-reducing bunds and/or barriers as per Conditions 16 and 18).	Section 3, and Appendix C
The best practicable means which will be used to control noise and vibration levels on site including such measures proposed in the Environmental Statement and Supplementary Environmental Information. Such measures shall include, but are not limited to: the use of the quietest available plant, equipment and techniques; the regular maintenance and inspection of such plant and equipment; the use of cladding, attenuators and barriers to reduce noise levels from noisy plant and operations; the specification of appropriate reversing alarms to minimise annoyance; and, measures to reduce vibration and air overpressure during blasting.	Section 5
Details of the noise and vibration monitoring system to be installed around the DNF and LCP sites to continuously log noise levels during construction and operation. The system shall include at least six noise monitors installed around the boundary of the Dove's Nest site and at least four monitors at key residential receptors near the Dove's Nest site and at least four noise monitors around the Lady Cross Plantation Site and at least three monitors at key residential receptors near the Lady Cross Plantation site.	Section 4

NYMNPA 18	Compliance with Condition NYMNPA-18
<p>The precise number and location of noise monitors shall be set out in the NVMP. The developer shall use reasonable endeavours to obtain access to the residential receptor properties for the installation of noise monitors and only if access cannot be obtained the number or location of noise monitors may be reduced. The MPA and the SBC EHO and/or their advisers shall be granted access to inspect the noise and vibration data whenever required, records of the data should be kept for a reasonable period and these records should be accessible by the public.</p>	<p>Section 3, Section 4 and Figure B.1</p>
<p>Details of the procedure to be followed in the event that the noise predictions detailed in the NVMP or the noise limits detailed in conditions 16 to 19 are exceeded. Such procedures shall require the investigation of the reasons for the breach of the limits and the cessation of the activity causing the breach until such a time as additional mitigation can be provided.</p>	<p>Section 5.4</p>
<p>Details of how the residents will be informed and consulted about the site operations and progress, particularly in regard to blasting and especially noisy operations including details of complaints logging and management procedures and a 24-hour telephone incident hotline. Details of the procedure for investigating complaints and informing complainants of the results of such investigations and of any actions resulting from them.</p>	<p>Section 5.4</p>
<p>The NVMP shall be adhered to at all times unless agreed previously in writing by the MPA.</p>	<p>A document sign off section has been included within this report requiring the Contractor to commit to compliance with the NVMP</p>
<p>The NVMP shall be updated and agreed whenever appropriate to reflect changes in the programme during construction and operation and at intervals not less than 6 months after the initial start on site and thereafter annually.</p>	<p>Section 1</p>

1.1.3 This NVMP relates to the Phase 7 Works at Woodsmith Mine and does not include any activities at Lady Cross Plantation, as these works have been deferred. The NYMNPA has confirmed that it supports this approach.

1.1.4 Phase 5 and 6 activities will continue past the start date of Phase 7. This NVMP therefore supersedes all previous NVMPs upon the commencement of Phase 7 and considers processes and controls with respect to all activities on site throughout Phase 7. Activities required for Phase 7 comprise the following:

- Completion of Service Shaft Headgear Chamber;
- Completion of Service Shaft to 83.17m AOD via Vertical Shaft-Sinking Machine (VSM) Method;
- Excavation of Production Shaft Headgear Chamber;
- Excavation from base of Production Shaft Headgear Chamber to 83.66m AOD;
- Surface Water Run-Off Silt Treatment Facility Building;
- Erection of temporary facilities to enable mobilisation of deep shaft sinking contractor;
- Earthworks and drainage; and
- Contingency grouting of the MTS Shaft (if required).

Planning Conditions

- 1.1.5 In addition to Condition NYMNPA 18, two further conditions NYMNPA 20 and NYMNPA 21 establish noise limits relating to the Woodsmith Mine site (see **Section 2.2**). Conditions NYMNPA 24, 27, 28 and 29 relate to vibration arising from blasting activities underground chamber construction.
- 1.1.6 In this document, the term “*construction*” includes all physical and related engineering and construction activities associated with the Phase 7 Works, as described above. Updates to this plan will be prepared and submitted to the NYMNPA for approval in advance of subsequent construction phases and following any material design or method change.

2 GUIDANCE

2.1 Legislation and British Standards

2.1.1 As a minimum, the Contractor will adhere to the following standards:

- BS 7445:2003 *Description and measurement of environmental noise*; and
- BS 5228:2009+A1:2014 *Code of Practice for noise and vibration control on construction and open sites*.

2.2 Construction Limits

2.2.1 Established construction noise limits (as measured at the identified receptors) remain as:

- 55 dB $L_{Aeq,1hr}$ for daytime (07:00 – 19:00);
- 65 dB $L_{Aeq,1hr}$ for the demolition of buildings and erection of new structures;
- Up to 70 dB $L_{Aeq,1hr}$ for temporary noisy operations to provide noise-reducing earth bunds and / or barriers; and
- 42 dB $L_{Aeq,1hr}$ for evening and night-time (19:00 – 07:00).

2.3 Construction Method

2.3.1 Contractors associated with the Phase 7 Works (see Construction Environmental Management Plan (CEMP; reference 40-RHD-WS-70-EN-PL-0029)) have provided details of the construction masterplan, number and type of plant items to be used and location/duration of construction activities within the site. The Construction Method Statement for the Phase 7 Works (reference 40-SMP-WS-7100-PA-MS-00003) outlines the proposed approach.

2.3.2 **Appendix C** details the plant items used within the model, their sound power level and location on site. Predictions of noise levels based upon these details are assessed within this NVMP.

3 PREDICTED CONSTRUCTION NOISE AND VIBRATION LEVELS

3.1 Baseline Receptor Locations

3.1.1 Residential and recreational receptors for this NVMP remain as identified in the Environmental Statement (ES) which accompanied the planning application, in previous iterations of the NVMP (e.g. Phase 4 NVMP; document reference 40-RHD-WS-70-EN-PL-0017), and as shown in **Figure B1 (Appendix B)**.

3.2 Predicted Noise Levels

3.2.1 Noise modelling was undertaken to provide predictions of noise levels throughout the Phase. **Tables C.1 and C.2 in Appendix C** outline the construction noise assessment predictions for the Phase 7 Works.

3.2.2 Noise levels due to construction activities in the Phase 7 Works were not predicted to exceed the agreed construction noise limits at any of the identified noise-sensitive receptors during the daytime, evening or night-time following the application of suitable measures, including phasing and physical mitigation.

3.3 Vibration

3.3.1 In relation to all other construction works ground borne vibration was considered according to the conservative approach outlined in previous NVMPs (e.g. Phase 4 document reference 40-RHD-WS-70-EN-PL-0017; see Table C.7, Appendix C for minimum set-back distances for vibration levels of reportable significance).

3.3.2 All identified sensitive receptors are at least 180m from the nearest site boundary, and the minimum distance between the primary haul route and any of the surrounding receptors is over 400m. Therefore ground-borne vibration levels will be below levels considered to be *“just about perceptible in residential environments”*¹.

¹ Planning Policy Guidance Note 24 (PPG24, 1994), Department for Communities and Local Government

4 NOISE MONITORING PROGRAMME

4.1 Noise Monitoring

- 4.1.1 Continuous noise monitoring, as required by condition NYMNPA 18, is being undertaken during construction at three key residential receptor locations and seven boundary locations as described in previous NVMP (e.g. Phase 4 document reference 40-RHD-WS-70-EN-PL-0017) and shown in **Appendix B, Figure B1**.
- 4.1.2 Monitoring commenced at each location on 04 April 2017 and continues to operate in compliance with relevant guidance as outlined in previous NVMPs (e.g. Phase 4 document reference 40-RHD-WS-70-EN-PL-0025). The Sound Level Meters (SLMs) record L_{Aeq} , L_{Amax} , L_{A90} , and L_{A10} data with a “fast” time constant and A-weighting (see **Appendix A** for descriptions of these terms). Weather condition monitoring is carried out simultaneously.
- 4.1.3 A system of real time alerts allows remote monitoring of noise levels. Alerts are managed by the Contractors, who respond to any potential breaches appropriately. Reports are produced monthly for submission to SBC and NYMNPA, confirming the measured noise data at each location and cross-referencing to corresponding weather data and Works Contractor Site Activity Logs. The full dataset is presented in graphical format.

5 MITIGATION AND PROCEDURES

5.1 Purpose of the Section

- 5.1.1 This section outlines measures to be taken by the Contractors to limit, and manage the impact of, noise. This section also outlines the Best Practicable Means and specific mitigation actions to be adopted.

5.2 Best Practice Measures

- 5.2.1 The Control of Pollution Act (1974) and BS 5228:2009+A1:2014 define working methods and mitigation measures referred to as Best Practicable Means (BPM). Appropriate BPM, set out in previous NVMPs (e.g. Phase 4, reference 40-RHD-WS-70-EN-PL-0017), will continue to be applied to the Phase 7 Works.

Management Structure and Responsibilities

- 5.2.2 While overall responsibility for compliance with environmental and approvals requirements will remain with Sirius Minerals, all Contractors working on site are accountable for undertaking the construction activities in line with the requirements of this NVMP.
- 5.2.3 The CEMP (reference 40-RHD-WS-70-EN-PL-0029) provides details of the lines of responsibility for environmental management (including relating to robust implementation of noise management and mitigation measures) during the Phase 7 Works.

Maintenance

- 5.2.4 Maintenance of plant will be carried out routinely and in accordance with the manufacturers' guidance. Daily inspections will be undertaken as described in previous NVMPs (e.g. Phase 4, reference 40-RHD-WS-70-EN-PL-0017).

Training

- 5.2.5 The site induction programme and site rules will include good working practice instructions for site staff, managers, visitors and contractors to help minimise noise, as set out in previous NVMPs (e.g. Phase 4, reference 40-RHD-WS-70-EN-PL-0017).

5.3 Specific Mitigation

Bunds

- 5.3.1 The bunds to the north and north east of the platform area now form a continuous barrier following the closure of the access gap. Additional bund creation to the north-east of the site will take place during Phase 7.

Activity timing, barriers, screens and enclosures

- 5.3.2 Temporary screens of 3m in height will be placed behind the diaphragm walling cutters (screens are demountable, to enable positioning at the side of the cutters facing receptor NM1). Screens will also be placed around the upper parts of the bentonite plant, thereby enclosing the vibrating screens.
- 5.3.3 Excavator-mounted rock breakers will be fitted with proprietary muffling devices to achieve a reduction in noise level of at least 10 dB(A).
- 5.3.4 A continuous barrier of 6m in height (comprising double stacked RAL 6008 shipping containers with an absorptive treatment to the inner face) will remain erected to the north and east of the Production Shaft, Service Shaft and MTS Shaft. Due to the further bund creation to the north east of the site during Phase 7 and the removal of diesel generators from the central area of the site, the continued requirement for this barrier will be assessed during Phase 7.

5.4 Communications

Procedure for complaints or breach of limits

- 5.4.1 The procedures to be followed in the event of a complaint or a breach of permitted noise limits will remain as set out in previous NVMPs (e.g. Phase 4, reference 40-RHD-WS-70-EN-PL-0017).

Public relations

- 5.4.2 Good public relations with local residents in nearby noise-sensitive receptors will be maintained.
- 5.4.3 A Community and Stakeholder Engagement Plan is provided in Appendix 4 to the Phase 3 CEMP (40-RHD-WS-70-EN-PL-0014). It remains valid for Phase 7 Works, and details actions to be taken by Sirius Minerals plc and the Contractors.

Appendix A Acoustic Terminology



Term	Definition
Noise sensitive receptors	People, property or designated sites for nature conservation that may be at risk from exposure to noise and vibration that could potentially arise as a result of the proposed development/project
Noise and Vibration study area	The area assessed for noise and vibration impacts during this assessment
Baseline scenario	Scenarios with the proposed development/project not in operation
Decibel (dB)	A unit of noise level derived from the logarithm of the ratio between the value of a quantity and a reference value. It is used to describe the level of many different quantities. For sound pressure level the reference quantity is 20 μ Pa, the threshold of normal hearing is 0dB, and 140dB is the threshold of pain. A change of 1dB is only perceptible under controlled conditions. Under normal conditions a change in noise level of 3dB(A) is the smallest perceptible change.
dB(A)	Decibels measured on a sound level meter incorporating a frequency weighting (A weighting) which differentiates between sounds of different frequency (pitch) in a similar way to the human ear. Measurements in dB(A) broadly agree with people's assessment of loudness. A change of 3 dB(A) is the minimum perceptible under normal conditions, and a change of 10 dB(A) corresponds roughly to halving or doubling the loudness of a sound. The background noise level in a living room may be about 30 dB(A); normal conversation about 60 dB(A) at 1 metre; heavy road traffic about 80 dB(A) at 10 metres; the level near a pneumatic drill about 100 dB(A).
$L_{Aeq,T}$	The equivalent continuous sound level – the sound level of a notionally steady sound having the same energy as a fluctuating sound over a specified measurement period (T). $L_{Aeq,T}$ is used to describe many types of noise and can be measured directly with an integrating sound level meter.
$L_{A10,T}$	The A weighted noise level exceeded for 10% of the specified measurement period (T). L_{A10} is the index generally adopted to assess traffic noise
$L_{A90,T}$	The A weighted noise level exceeded for 90% of the specified measurement period (T). In BS 4142:2014 it is used to define the 'background' noise level.
L_{Amax}	The maximum A-weighted sound pressure level recorded during a measurement.
PPV	Instantaneous maximum velocity reached by a vibrating element as it oscillates about its rest position.
'A' weighting	A frequency weighting to compensate for the varying sensitivity of the human ear to sound at different frequencies.
Fast time constant	Sound level meters have two conventional time weightings, F = Fast and S = Slow with time constants of 125 ms and 1000 ms respectively. Fast time constant relates to the response time of the meter which allows rapid variations in noise level to be registered.



Appendix B Figures



Page intentionally blank

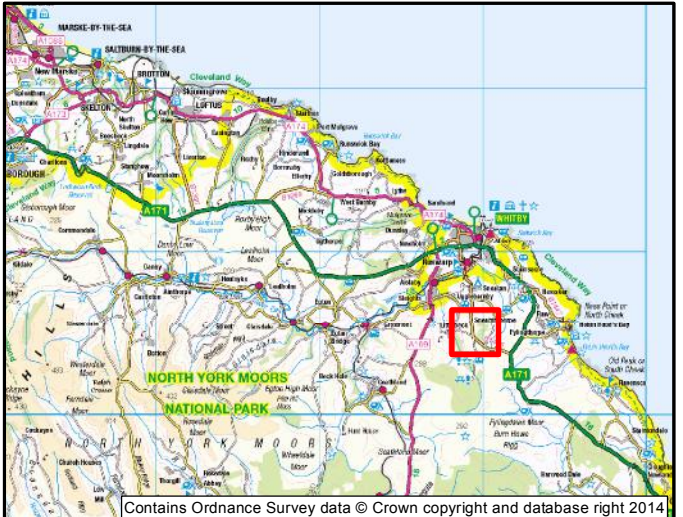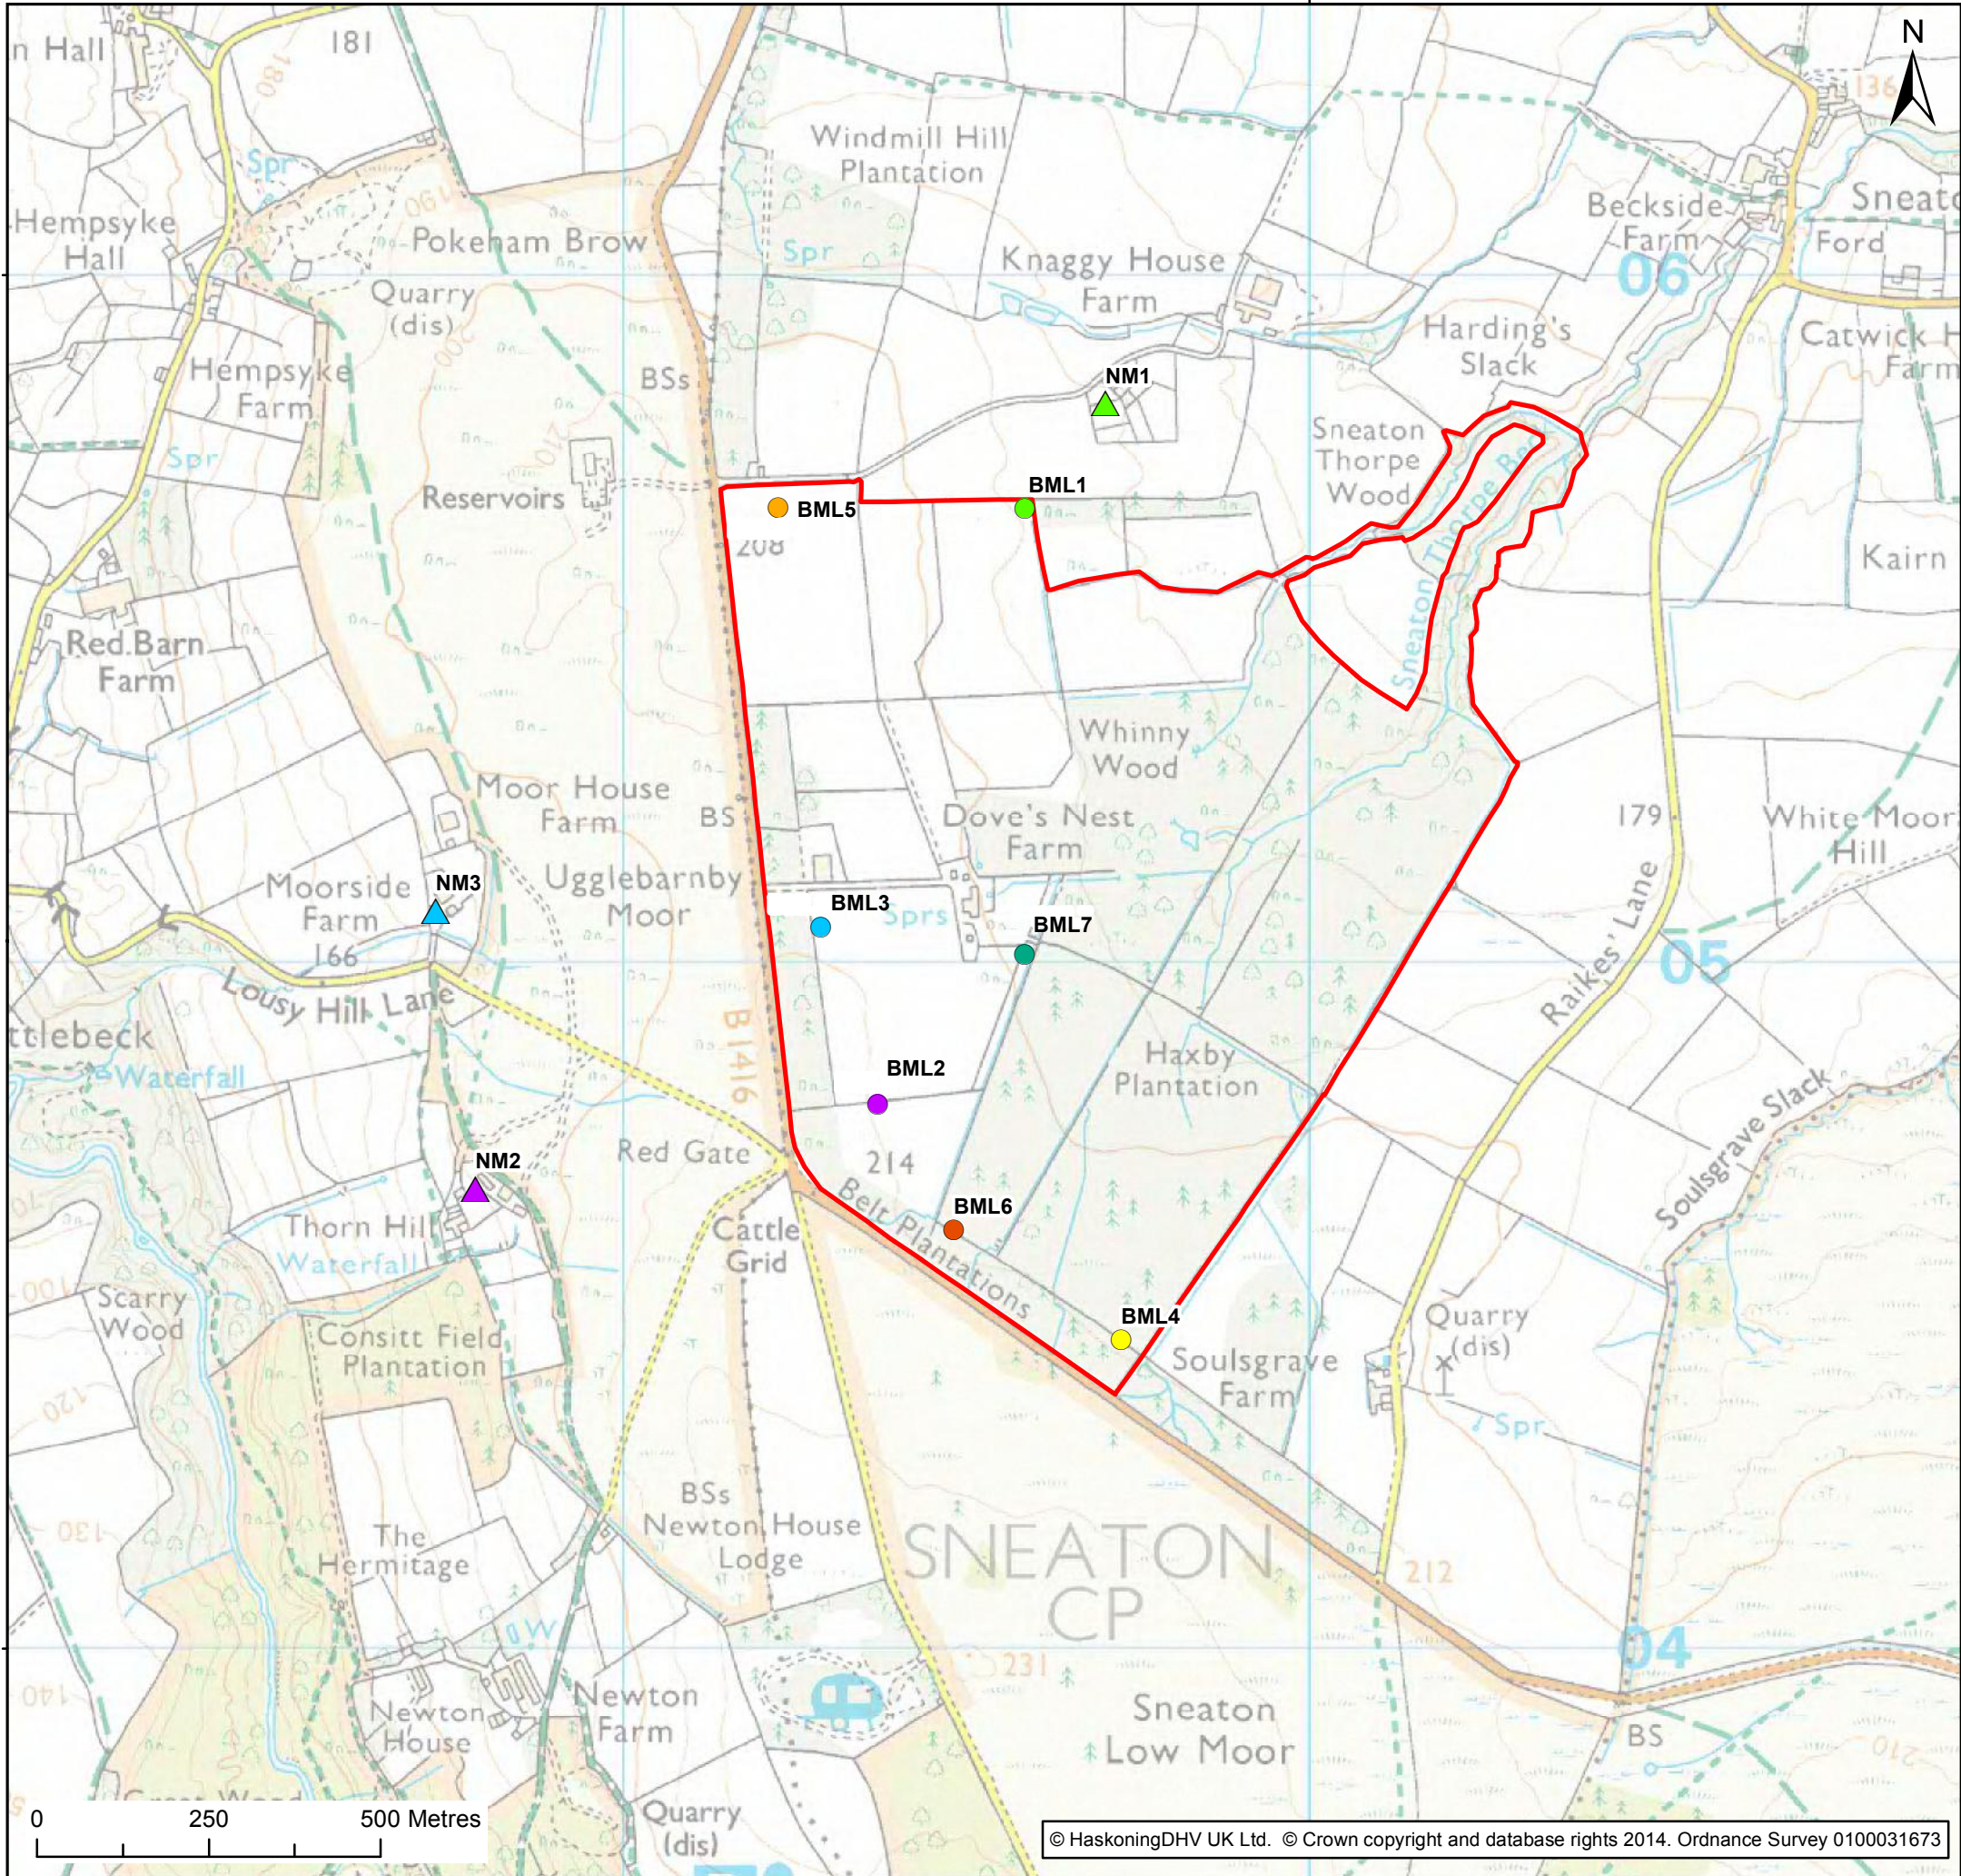

- Legend:
- Land Ownership Boundary
 - Receptor Monitoring Locations**
 - ▲ NM1 - Parkdown Bungalow
 - ▲ NM2 - Thornhill
 - ▲ NM3 - Moorside Farm
 - Site Boundary Monitoring Locations**
 - BML1 - Parkdown Bungalow
 - BML2 - Thornhill
 - BML3 - Moorside Farm
 - BML4 - Soulsgrave Farm/Wainwright Coast to Coast Walk
 - BML5 - Lound House
 - BML6 - Sneaton Foss/Falling Foss
 - BML7 - Between shaft sinking area and BML4

Client:	Project:
Sirius Minerals plc	Sirius North Yorkshire Polyhalite Project

Title: Proposed Residential Receptor and Boundary Noise Monitoring Locations

Appendix: A	Figure: A.1	Drawing No: 40-RHD-WS-70-EN-PL-0016-D001
Rev: A	Date: 08/09/2017	Drawn: DC
	Checked: AB	Size: A3
		Scale: 1:10,000

Co-ordinate system: British National Grid

ROYAL HASKONINGDHV
INDUSTRY AND BUILDINGS
 RIGHTWELL HOUSE
 BRETTON
 PETERBOROUGH
 PE3 8DW

Enhancing Society Together

Appendix C Predicted Construction Noise Levels

The predicted noise levels detailed within the tables below are considered to represent the most conservative scenario.

Table C.1 Calculated highest noise levels during Phase 7 – Daytime

Receptor Location	Daytime (07:00–19:00)	
	Limit $L_{Aeq,1hr}$ dB	Maximum Predicted $L_{Aeq,1hr}$ dB
Parkdown Bungalow	55	51.6
Moor House Farm	55	49.0
Moorside Farm	55	47.7
Thornhill	55	46.9
Soulsgrave	55	46.8
Wainwright Coast to Coast Path	55	47.4
Sneaton Foss Caravan Park	55	46.2
Falling Foss Tearooms	55	33.5
Lound House Caravan Park	55	46.9

Table C.2 Calculated highest noise levels during Phase 7 – Evening and night time

Receptor Location	Evening and Night-time (19:00–07:00)	
	Limit L _{Aeq,1hr} dB	Maximum Predicted L _{Aeq,1hr} dB
Parkdown Bungalow	42	40.2
Moor House Farm	42	37.8
Moorside Farm	42	36.6
Thornhill	42	35.9
Soulsgrave	42	39.3
Wainwright Coast to Coast Path	42	37.7
Sneaton Foss Caravan Park	42	37.4
Falling Foss Tearooms	42	21.7
Lound House Caravan Park	42	35.3

During the past year, visits have been made to the various receptors for equipment maintenance and monitoring purposes. At those receptors to the south and west of the site (particularly Moorside, Thornhill and the Wainwright Coast to Coast Path) it was observed, over a number of visits, that site noise is generally inaudible. Predicted noise levels in the tables above can, therefore, be considered a very conservative case.

Modelling Assumptions

The following equipment and associated sound power levels were used within the SoundPLAN noise models:

Diaphragm Walling (Production Shaft)

- 1no. MC128 Diaphragm Walling Rig, measured 110 dB(A), 100% ontime
- 2no. MC96 Diaphragm Walling Rigs, measured 108 dB(A) 100% ontime (Production Shaft)
- Crawler crane, 1no. 90t Kobelco CKE900G or similar, 110 dB(A) daytime only
- Crawler crane, 1no. 160t Liebherr LR1160 or similar, 105 dB(A) daytime only
- Mobile crane, 110t Liebherr LTM 1100 or similar, 110 dB(A) daytime only

Vertical Shaft Sinking (Service Shaft)

- 1x Vertical Shaft Sinking Machine (surface equipment including hydraulic winches) – 101 dB(A)

1 x 1MW Generator – 108.1 dB(A) (on standby)
 1 x Desander – 108.1 dB(A)
 1x Mobile crane, 110t Liebherr LTM 1100 or similar, 110 dB(A)
 1x front end loader – 109 dB(A) CAT 966M or similar

Vertical Shaft Sinking (MTS Shaft)

1x Vertical Shaft Sinking Machine (surface equipment including hydraulic winches) – 101 dB(A)
 1 x 1MW Generator – 108.1 dB(A) (on standby)
 1 x Desander – 108.1 dB(A)
 1x Mobile crane, 110t Liebherr LTM 1100 or similar, 110 dB(A)
 1x front end loader – 109 dB(A) CAT 966M or similar
 3x Tower Lights, 85 dB(A)

Excavation of foreshaft

2x 22t Excavator mounted muffled rock breakers, 111 dB(A) daytime only
 1x 35t Excavator moving rubble, 114 dB(A) daytime only
 4x ATD, 109 dB(A)
 4x Tower Lights, 85 dB(A)
 1x Crawler Crane, 110 dB(A)
 1x Mobile Crane, 110 dB(A)
 160kVA Generator, 86 dB(A)
 1x Concrete Truck discharging, 111.6 dB(A)
 2x Drill rigs, 114 dB(A)
 2x Poker Vibrators, 112 dB(A)
 1x Dump truck being loaded, 115 dB(A)
 1x Bulk skip filling, 114 dB(A)

Silt Treatment Facility Building

1x Mobile Crane, 110 dB(A) for steel frame erection (daytime only)
 3x 25t Excavator moving rubble, 114 dB(A)
 1x Dump truck being loaded, 115 dB(A)

MTS Hydraulic Rotary Piling

1x Soilmec SR40

Contingency Grouting of the MTS Shaft

1x Geotechnical Drilling rig, 77 dB(A)
 1x Flush Recirculation pump, 54 dB(A)
 1x Desanding unit, 54 dB(A)
 1x Water Treatment Plant, 67 dB(A)
 1x Grout Mixing & Injection Plant, 60 dB(A)
 1x Pressure Washer, 75 dB(A)
 1x Compressor, 75 dB(A)

Other

1x Lime Plant – 107 dB(A)
 1x Crusher – 109 dB(A)

Mobile equipment was modelled as a moving point line source with speeds of between 5 and 20 kph.
 Stationary plant was modelled as a point source.



Noise propagation was calculated using the BS 5228:2009+A1:2014 methodology.
